

## Beam Profile Measurement at A171 Flag

A. S. Carroll

August 1980

Collider Accelerator Department  
**Brookhaven National Laboratory**

**U.S. Department of Energy**

USDOE Office of Science (SC)

Notice: This technical note has been authored by employees of Brookhaven Science Associates, LLC under Contract No.DE-AC02-76CH00016 with the U.S. Department of Energy. The publisher by accepting the technical note for publication acknowledges that the United States Government retains a non-exclusive, paid-up, irrevocable, world-wide license to publish or reproduce the published form of this technical note, or allow others to do so, for United States Government purposes.

## **DISCLAIMER**

This report was prepared as an account of work sponsored by an agency of the United States Government. Neither the United States Government nor any agency thereof, nor any of their employees, nor any of their contractors, subcontractors, or their employees, makes any warranty, express or implied, or assumes any legal liability or responsibility for the accuracy, completeness, or any third party's use or the results of such use of any information, apparatus, product, or process disclosed, or represents that its use would not infringe privately owned rights. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors. The views and opinions of authors expressed herein do not necessarily state or reflect those of the United States Government or any agency thereof.

Date 8/5/80 Time 12:00-13:00 Experimenters A.S. Carroll, B. Ewing and J.W. Glenn III  
Subject Beam Profile Measurements at A 171 Flag

OBSERVATIONS AND CONCLUSION

Introduction

This report describes a beam profile measurement at the A 171 flag box by activation of aluminum foils. These measurements were done to check the beam size near the site of the D-line superconducting magnets under actual SEB operating conditions.

AGS Conditions

The beam split at the time of the activation was A line -  $3 \times 10^{12}$ , B line -  $1.3 \times 10^{12}$  and C line -  $.3 \times 10^{12}$ . The 3 mil aluminum foils were clipped at  $45^\circ$  with respect to the vertical on to the front of the A 171 flag. The beam was run for 100 pulses corresponding to  $3.12 \times 10^{14}$  protons seen by the A line SEC. The beam was stable during the run.

Results

The beam profiles as measured by cutting the foil into 2 mm strips across the entire spot and correcting for foil weight and decay are shown in Fig. 1 and 2. Unfortunately the vertical profile is not complete due to placement of the foil but it seems reasonable to assume that the vertical profile is symmetric as shown by the dotted line.

Working from the quadrupole currents and AGS emittance measurements of H. Weisberg the predicted horizontal and vertical widths are as shown in the figures.

The horizontal widths containing 90% and 99% of the beam are 3.5 cm and 5.2 cm. The corresponding vertical profile heights are 2.9 cm and 6.8 cm.

Conclusions

The observed profile widths are considerably larger than predicted. Since the beam size at this point is of considerable importance to its operation of the D line superconducting magnets, further studies should be carried out in November.

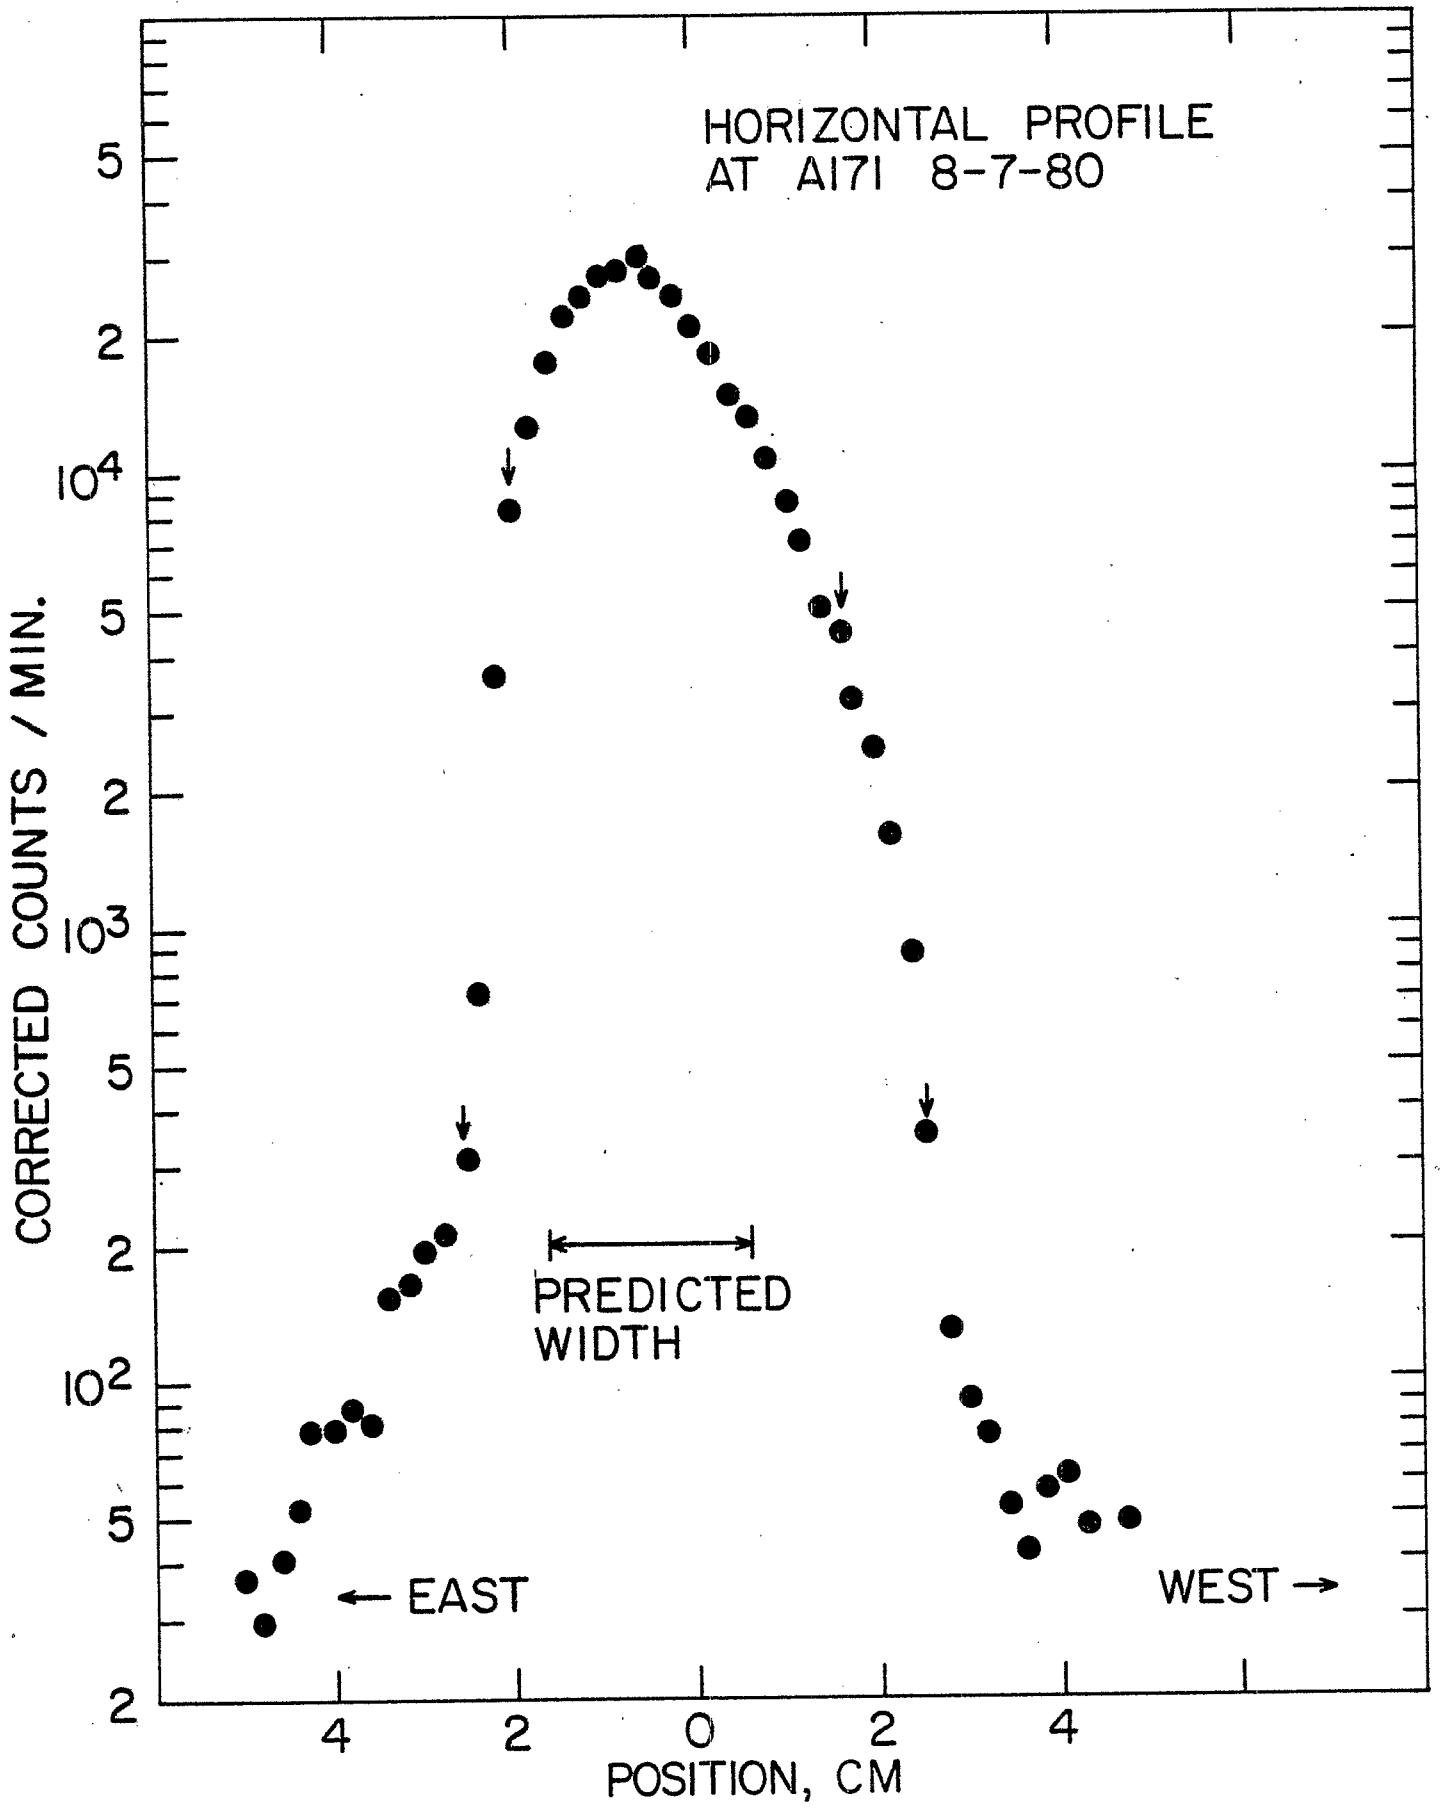


Fig. 1

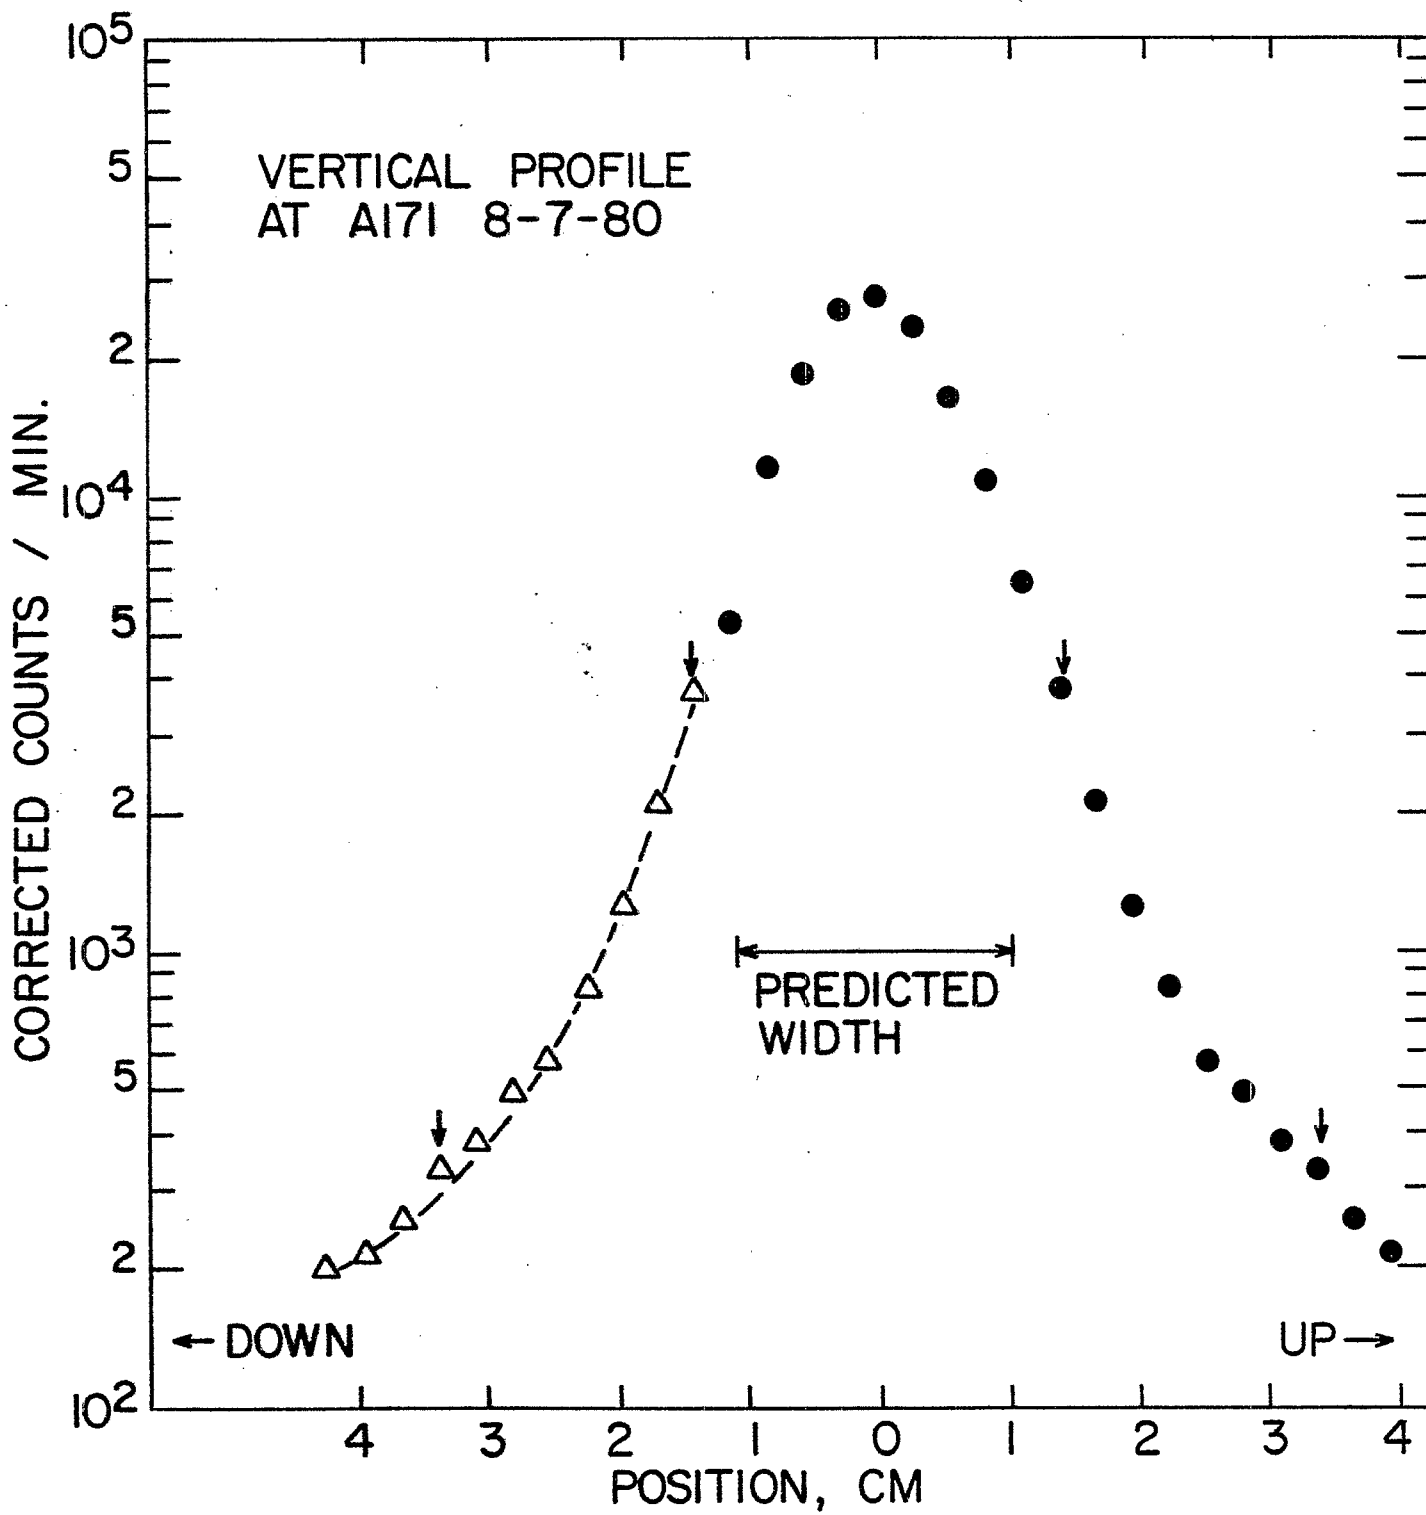


Fig. 2
