

BNL-104029-2014-TECH AGS.SN151;BNL-104029-2014-IR

Operation at Full B

M. Clancy

June 1983

Collider Accelerator Department

Brookhaven National Laboratory

U.S. Department of Energy

USDOE Office of Science (SC)

Notice: This technical note has been authored by employees of Brookhaven Science Associates, LLC under Contract No.DE-AC02-76CH00016 with the U.S. Department of Energy. The publisher by accepting the technical note for publication acknowledges that the United States Government retains a non-exclusive, paid-up, irrevocable, world-wide license to publish or reproduce the published form of this technical note, or allow others to do so, for United States Government purposes.

DISCLAIMER

This report was prepared as an account of work sponsored by an agency of the United States Government. Neither the United States Government nor any agency thereof, nor any of their employees, nor any of their contractors, subcontractors, or their employees, makes any warranty, express or implied, or assumes any legal liability or responsibility for the accuracy, completeness, or any third party's use or the results of such use of any information, apparatus, product, or process disclosed, or represents that its use would not infringe privately owned rights. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors. The views and opinions of authors expressed herein do not necessarily state or reflect those of the United States Government or any agency thereof.

Number	151

AGS STUDIES REPORT

Date June 8 & 9, 1983		Time _	Day Shift	Day Shift	
Experimenters	M. Clancy, J. Gabusi	, E. Gill and	J.W. Glenn		
Reported by	J.W. Glenn Operation at Full B				

OBSERVATIONS AND CONCLUSION

Introduction

The Siemens power supply for the AGS main magnet was operated at full output. The potential for increasing the repetition rate was monitored. Beam was accelerated without a reduction in intensity.

Power Supply Setup

The Siemens set excitation was adjusted to provide the maximum allowed 7500 volt generator output. For "Save-a-Watt" pulsing, the output voltage was 2200 volts on the magnet at injection time, up from about 1600 volts. The injection peaker also moved 11 ms earlier to 38.5 ms. (This change was a bit smaller than scaling and a 5 ms turn on delay would imply.) The pulse length was then extended to achieve full current. The generator voltage, as read on the control station meter, appeared to rise a bit, so excitation was dropped 5% to stay within the 7500 volt limit. Full current was achieved by 741 ms, 121 ms earlier than normal B, and the dwell time increased by 200 ms. The set was then pulsed for half an hour and pictures taken. (Figures 1 and 2 are composites of early and late voltage and current waveform pictures.) The large ringing at the end of the high B cycle (Figure 2) was adjusted out on June 9, 1983 for acceleration tests.

Acceleration

The setup on June 8 was repeated on June 9 and beam was injected and accelerated. After some tuning, injected intensity was 18 TP, captured at 3 ms - 12 TP and accelerated to 100 ms - 9.5 TP. Bunching was normal (Figure 3). The IPM showed a slightly smaller beam size for the high B case, but when the time is normalized to B, and thus to momentum, the beam is slightly larger after the 75 ms transition out of the "front porch" (Figures 4 and 5) The beam was accelerated to approximately 27 GeV/c. The rf system tracked the higher B

without losses before transition. There was an erratic loss at transition time, but schedule pressure did not allow sufficient time to investigate it and/or tune it away.

Conclusions

- 1. This change did not significantly affect the amount of beam captured.
- 2. With this rate of rise, it would be possible to run the FEB program at a 1.2 second repetition period.


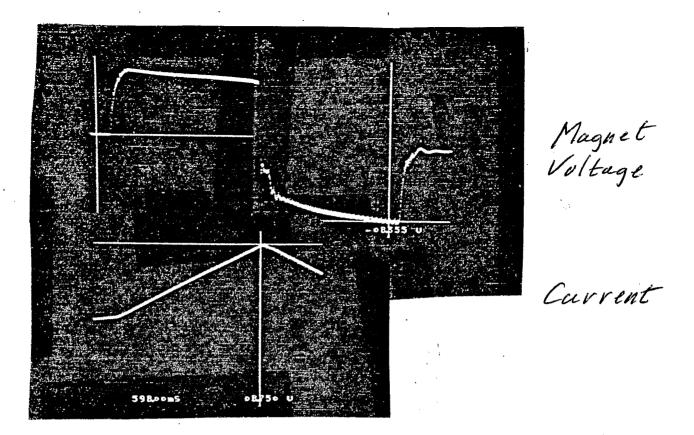



Fig 1 Mormal B

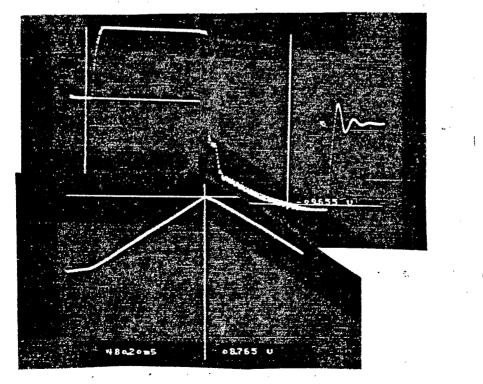

Magnet. Voltage

Current

Fig 2 High B

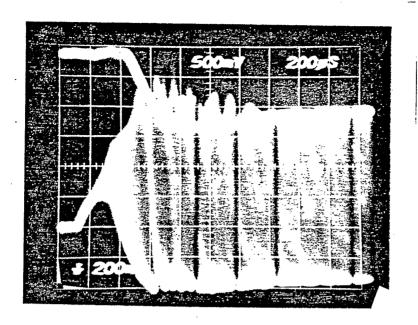

F20 Fast Beam Current Trans former

Fig 3 Beam Bunching

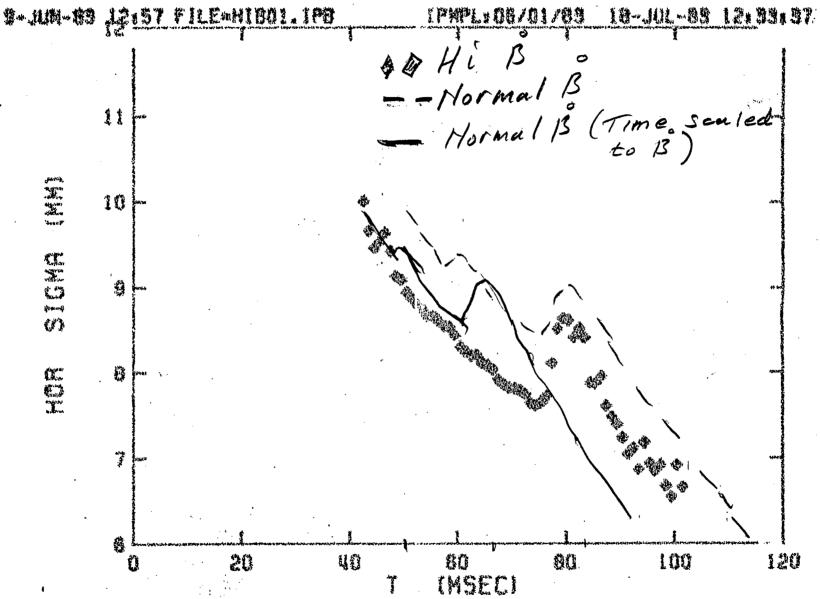


Fig 4. Horizontal Beam Size
