

Further Investigation of A-line transport losses

H. N. Brown

December 1977

Collider Accelerator Department
Brookhaven National Laboratory

U.S. Department of Energy

USDOE Office of Science (SC)

Notice: This technical note has been authored by employees of Brookhaven Science Associates, LLC under Contract No.EY-76-C-02-0016 with the U.S. Department of Energy. The publisher by accepting the technical note for publication acknowledges that the United States Government retains a non-exclusive, paid-up, irrevocable, world-wide license to publish or reproduce the published form of this technical note, or allow others to do so, for United States Government purposes.

DISCLAIMER

This report was prepared as an account of work sponsored by an agency of the United States Government. Neither the United States Government nor any agency thereof, nor any of their employees, nor any of their contractors, subcontractors, or their employees, makes any warranty, express or implied, or assumes any legal liability or responsibility for the accuracy, completeness, or any third party's use or the results of such use of any information, apparatus, product, or process disclosed, or represents that its use would not infringe privately owned rights. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors. The views and opinions of authors expressed herein do not necessarily state or reflect those of the United States Government or any agency thereof.

Date 12/2/77 Time 1200-1300 Experimenters H. Brown/J.W. GlennSubject Further investigation of A-line transport lossesOBSERVATIONS AND CONCLUSION

As the SEB was turned on for this period (on 11/22), CQ3 was moved 1/2" west to steer the A-line beam away from the AD1 septum. Also, the ring vertical bumps were turned on to reduce the losses on AD019 (the A/C splitter). Some of the tests on A-line transmission of 10/27 were repeated.

1) Varied A-line intensity between ~ 0 to $\sim 50\%$ of the total extracted beam. Delivery (A+B+C) only dropped by $\sim 7\%$. This implies ~ 1.15 protons toward A station needed to deliver one proton there. This is within the calibration errors of the SEC's (Fig. 1).

2) Swept beam across the entrance to AD1 with CD014. The transmission to A was near optimum. AD1 losses are within $\sim 15\%$ of minimum (Fig. 2).

3) Scanned beam vertically with CP033. Only a small reduction of AD1 loss was possible and at such a current that beam would not pass through the B/C splitter system (Fig. 3).

Conclusion: 1) Moving CQ3 to steer the beam toward the west seemed to reduce the losses on AD1 by a factor of ~ 2 . Further reduction of $\sim 20\%$ may be possible.

2) The delivery to A is significantly better (59% to $\sim 87\%$).

3) Vertical alignment is better though not perfect.

Recommendations:

1) The SEC's must have closer to identical response for further work.

2) Recommendations of Report #104 still are valid.

Note: During start-up AD1 was rolled as per Report #103. Beam was not observed at A station and the roll was removed. It is not known whether the roll caused this problem. This should be repeated more carefully.

Note on Figures:


A300F	≡	A SEC/CE010 SEC
AD1	≡	AD1 loss/CE010 SEC
AQ47S	≡	AD5-6 loss/CE010 SEC
DEL	≡	A+B+C SEC's/CE010 SEC

Editorial: The slow beam extraction and transport system will only work as well as the instrumentation shows. The calibrations of the SEC's and the added loss monitor has made possible the 10% improvement in performance over the last two weeks. Further good instrumentation is needed for further improvement. For example, B-line may be only 80% efficient in its transport.

Fig #1

DELIV US A 7-DEC-77 17:48 38.7 YA:DEL ,0= 600,100= 800

$$DEL = \frac{A+B+C}{C10}$$

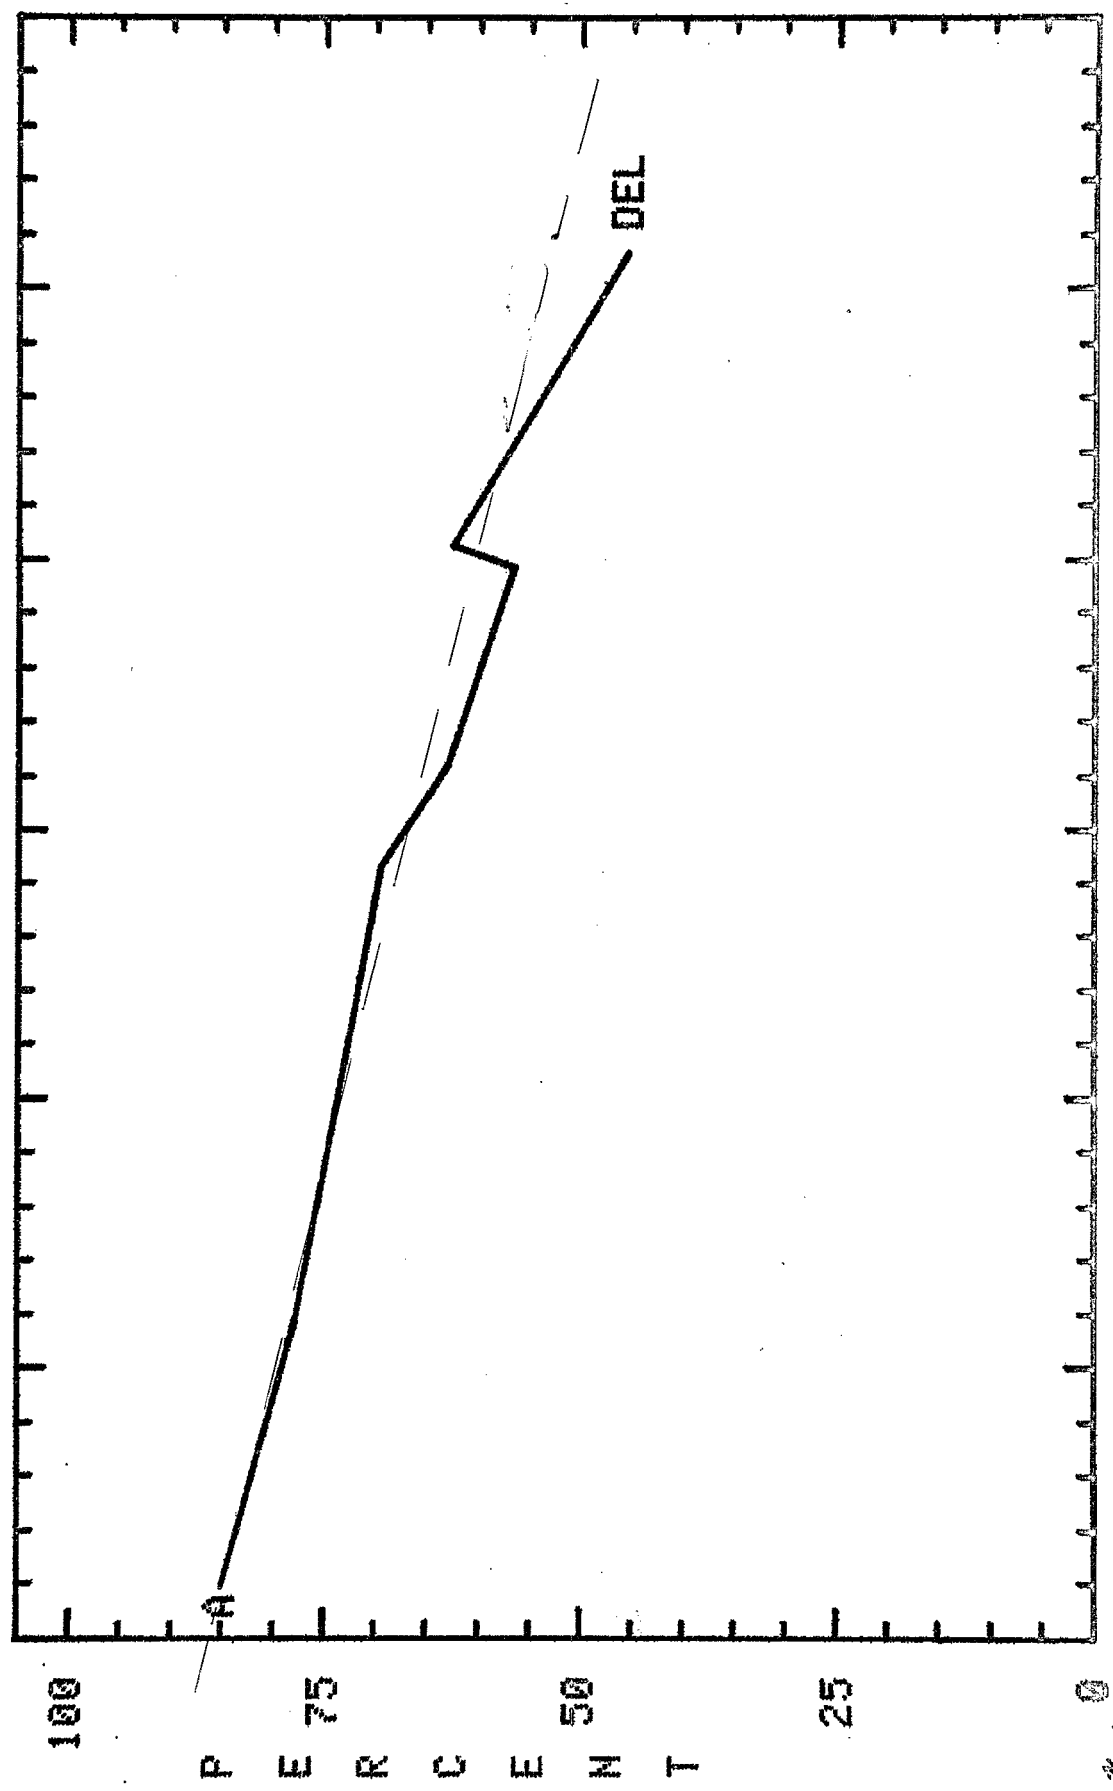

0.00 10.00 20.00 30.00 40.00 50.00
A300F X 10 PLOTS WHEN ABS(OLD-NEW) >=


Fig #2

A LOSSES AND EFF'S
7-DEC-77 16:15 50.8

YA:A300F,0=
YC:A047S,0=
YD:AD1,0=

0,100=
0,100=
0,100=

2000
1000
400

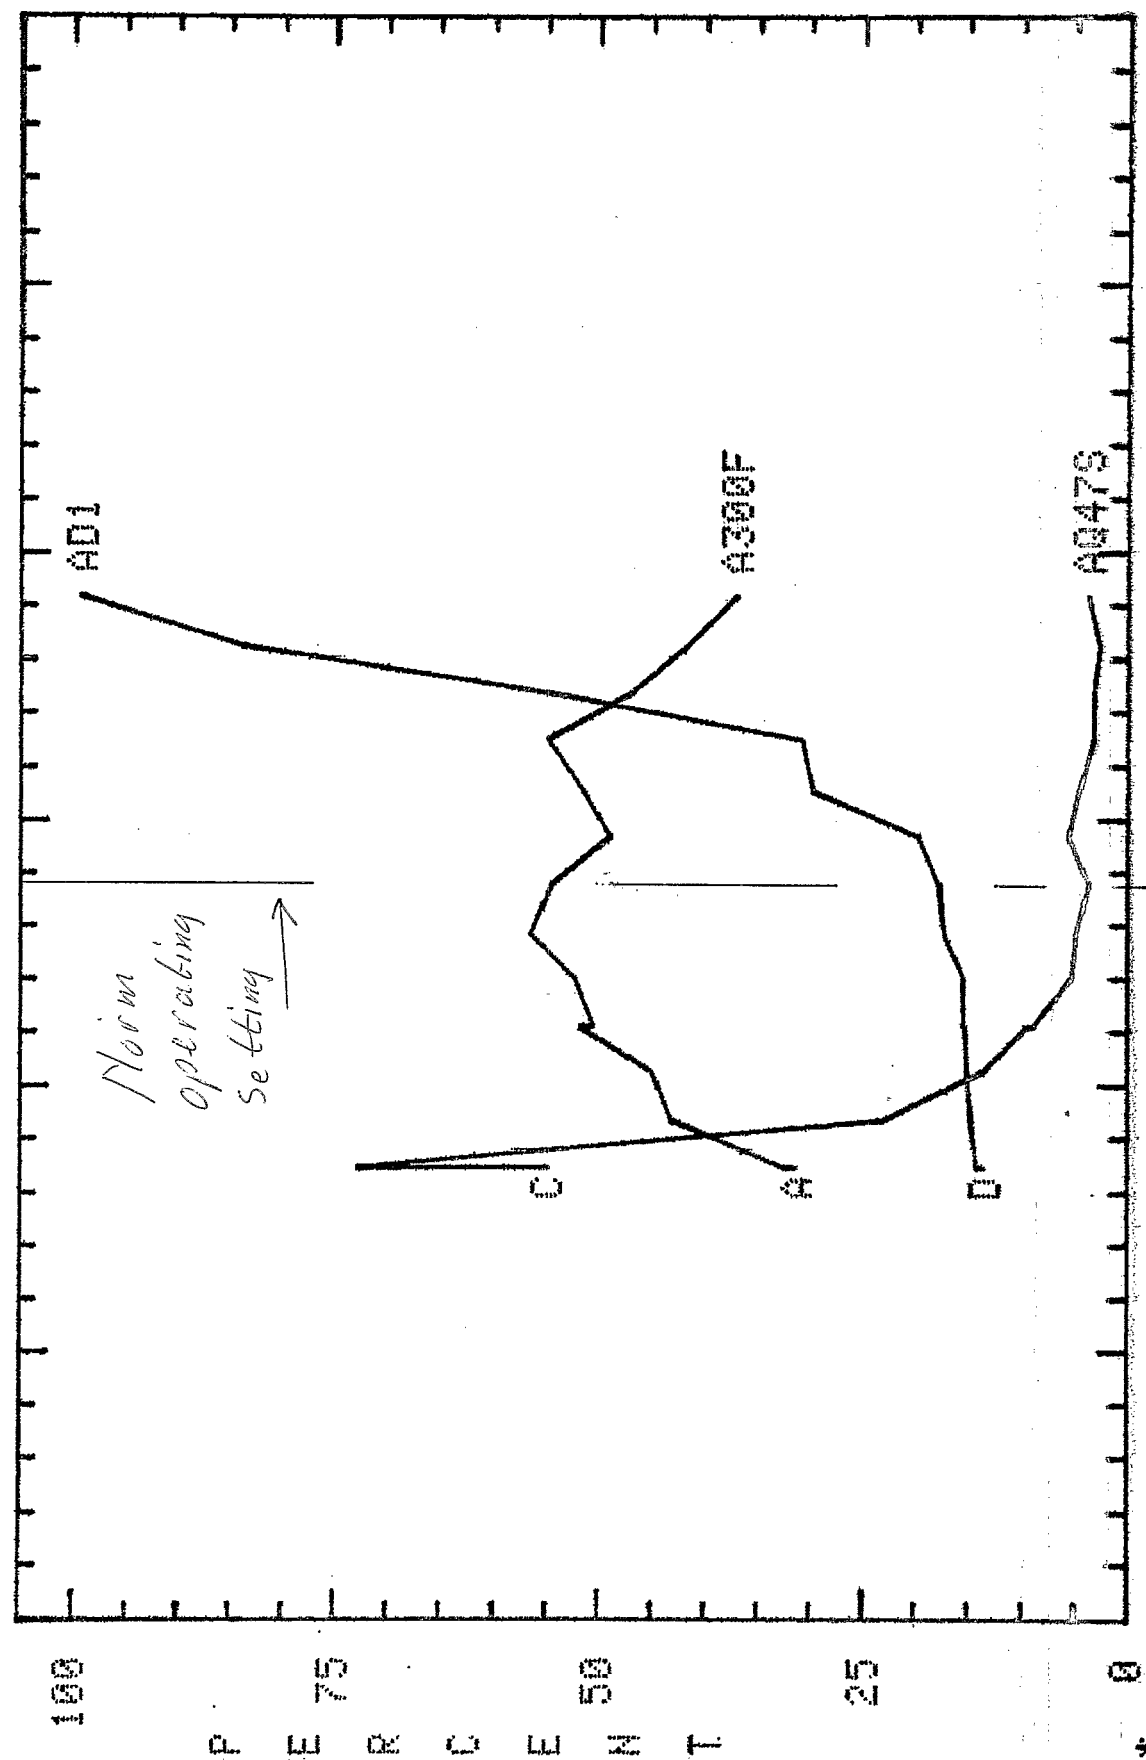

* -5.00 0.00 100 5.00 10.00 15.00 20.00
 CO014 X 100 PLOTS WHEN ABS(OLD-NEW) >= 0
 Moves Beam East →


Fig #5

A LOSSES AND EFF'S
7-DEC-77 16:07 33.6

YA:A300F,0=
YC:A047S,0=
YD:AD1,0=

0,100=
0,100=
-50,100=

2000
200
150

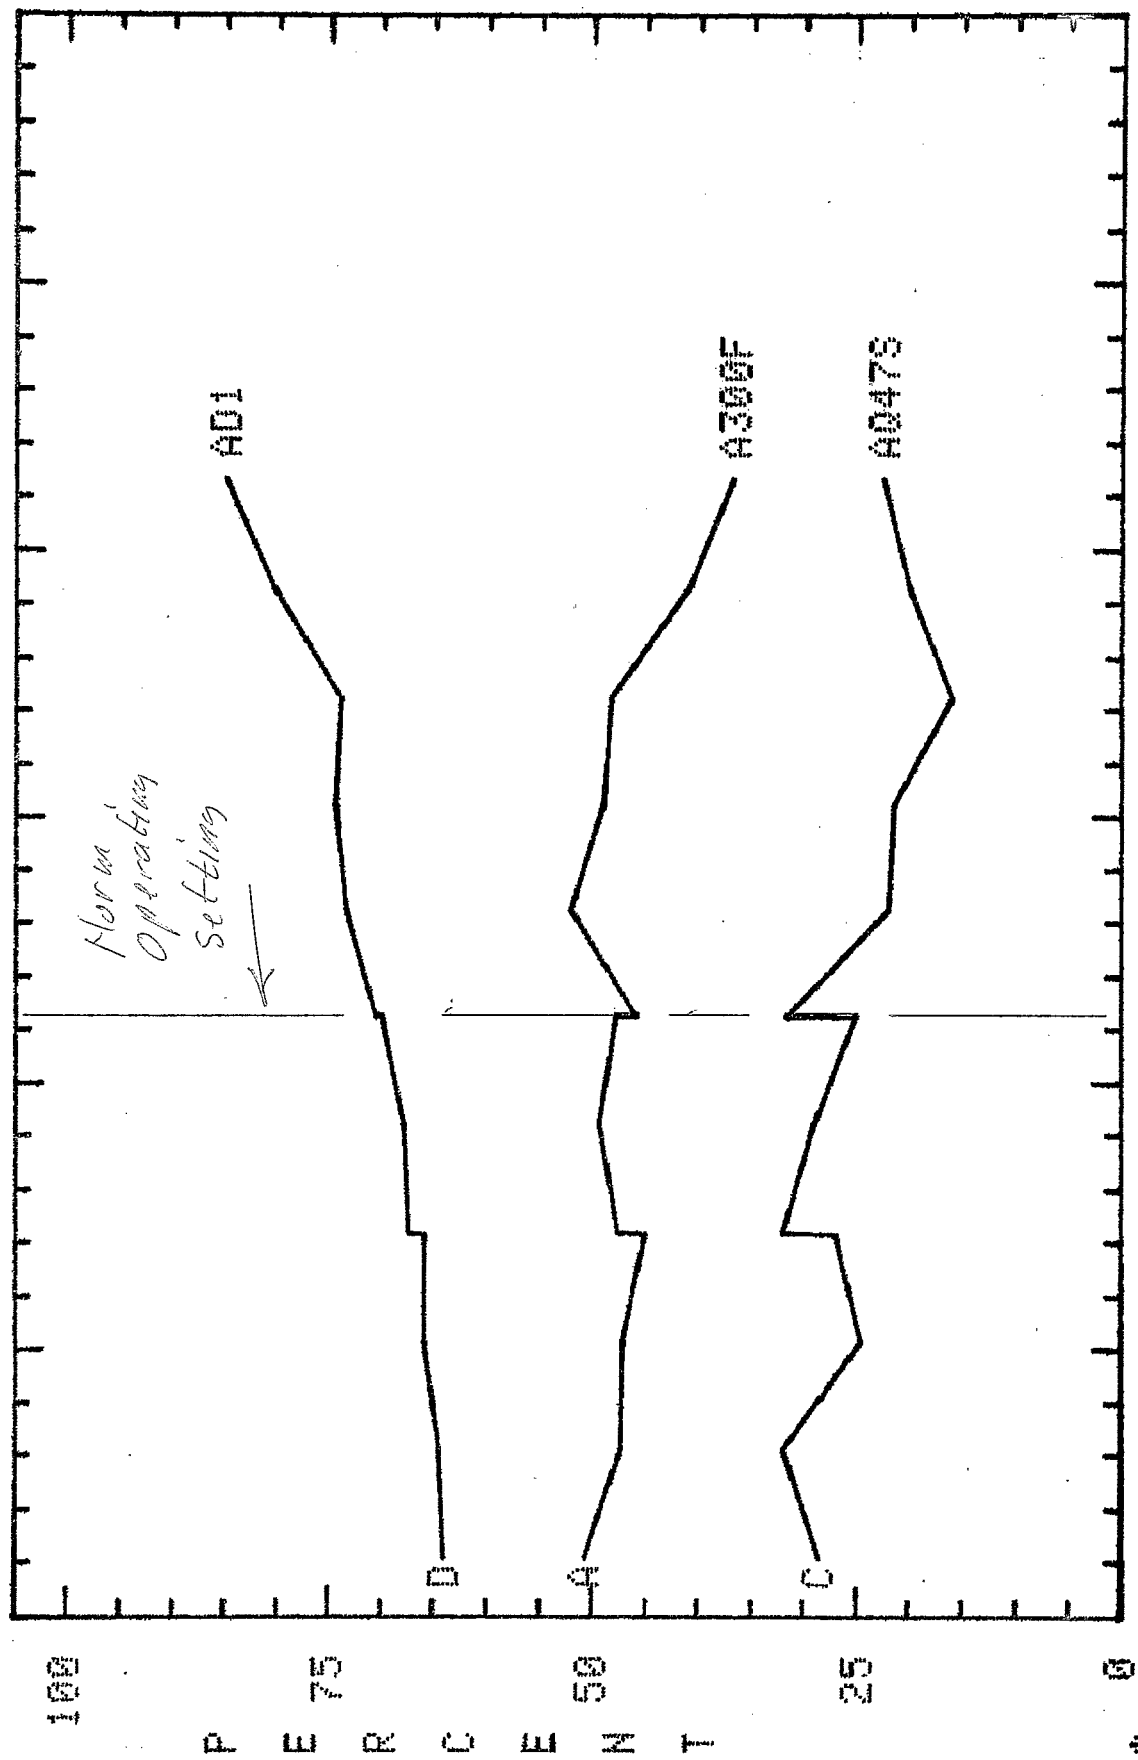

0.00 5.00 10.00 15.00 20.00 25.00
 CP033 X 100 PLOTS WHEN ABS(OLD-NEW) >= 0
 Macros Beam down at CF103
